



		Nombre	Duracion	Inicio	Terminado	Predecesores
1		☒ 1.0GESTIONDELPROYECTO	5 days	07/09/26,08:00	11/09/26,17:00	
2		Iniciacion y Planificacion del Proyecto (...)	5 days	07/09/26, 08:00	11/09/26, 17:00	
3		☒ 2.0ANALISISYREQUISITOS	8 days	07/09/26,08:00	16/09/26,17:00	
4		Analisis y Requisitos (elicitation, espec...	8 days	07/09/26, 08:00	16/09/26, 17:00	
5		HITO: SRS aprobado / Stage-Gate Fa...	0 days	16/09/26, 17:00	16/09/26, 17:00	2;4
6		☒ 3.0DISENO	15 days	17/09/26,08:00	07/10/26,17:00	
7		Arquitectura tecnica y diseno de BD/A...	6 days	17/09/26, 08:00	24/09/26, 17:00	5
8		HITO: Arquitectura lista (Semana 4)	0 days	24/09/26, 17:00	24/09/26, 17:00	7
9		Wireframes app movil y backoffice	6 days	17/09/26, 08:00	24/09/26, 17:00	5
10		Prototipo de alta fidelidad	5 days	25/09/26, 08:00	01/10/26, 17:00	9
11		Validacion y ajustes del prototipo	4 days	02/10/26, 08:00	07/10/26, 17:00	10
12		HITO: UX/UI y prototipo aprobado (Se...	0 days	07/10/26, 17:00	07/10/26, 17:00	11
13		Diseno de autentificacion y seguridad	3 days	25/09/26, 08:00	29/09/26, 17:00	7
14		☒ 4.0DESARROLLOEIMPLEMENTACION	47 days	25/09/26,08:00	30/11/26,17:00	
15		☒ 4.1 Backend	36 days	25/09/26,08:00	13/11/26,17:00	
16		Configuracion de entornos y base...	4 days	25/09/26, 08:00	30/09/26, 17:00	7
17		Autenticacion y gestion de usuari...	6 days	01/10/26, 08:00	08/10/26, 17:00	16
18		API de Mapa Interactivo (R6-R10)	7 days	09/10/26, 08:00	19/10/26, 17:00	17
19		API de Calendario Academico (R1...	6 days	20/10/26, 08:00	27/10/26, 17:00	18
20		API de Directorio y Notificaciones ...	7 days	28/10/26, 08:00	05/11/26, 17:00	19
21		Preparacion de datos institucional...	6 days	06/11/26, 08:00	13/11/26, 17:00	20
22		☒ 4.2 Movil	37 days	09/10/26,08:00	30/11/26,17:00	
23		Configuracion proyecto movil y au...	4 days	09/10/26, 08:00	14/10/26, 17:00	17
24		Desarrollo del mapa interactivo (m...	6 days	20/10/26, 08:00	27/10/26, 17:00	18;23
25		Desarrollo del calendario academi...	8 days	28/10/26, 08:00	06/11/26, 17:00	19;24
26		Desarrollo de directorio y notificac...	8 days	09/11/26, 08:00	18/11/26, 17:00	20;25
27		Integracion movil con Backend y p...	8 days	19/11/26, 08:00	30/11/26, 17:00	21;26
28		☒ 4.3 Web/Backoffice	35 days	09/10/26,08:00	26/11/26,17:00	
29		Configuracion backoffice y gestio...	5 days	09/10/26, 08:00	15/10/26, 17:00	17
30		Gestion de edificios, mapa y calen...	8 days	28/10/26, 08:00	06/11/26, 17:00	19;29
31		Gestion de directorio y notificacio...	8 days	09/11/26, 08:00	18/11/26, 17:00	20;30
32		Integracion con Backend y report...	6 days	19/11/26, 08:00	26/11/26, 17:00	21;31
33		HITO: Modulo Autenticacion y Mapa (...)	0 days	27/10/26, 17:00	27/10/26, 17:00	13;24;29
34		HITO: Beta cerrada (Semana 10)	0 days	18/11/26, 17:00	18/11/26, 17:00	26;31
35		HITO: Backoffice y ajustes de Beta (S...	0 days	26/11/26, 17:00	26/11/26, 17:00	21;32

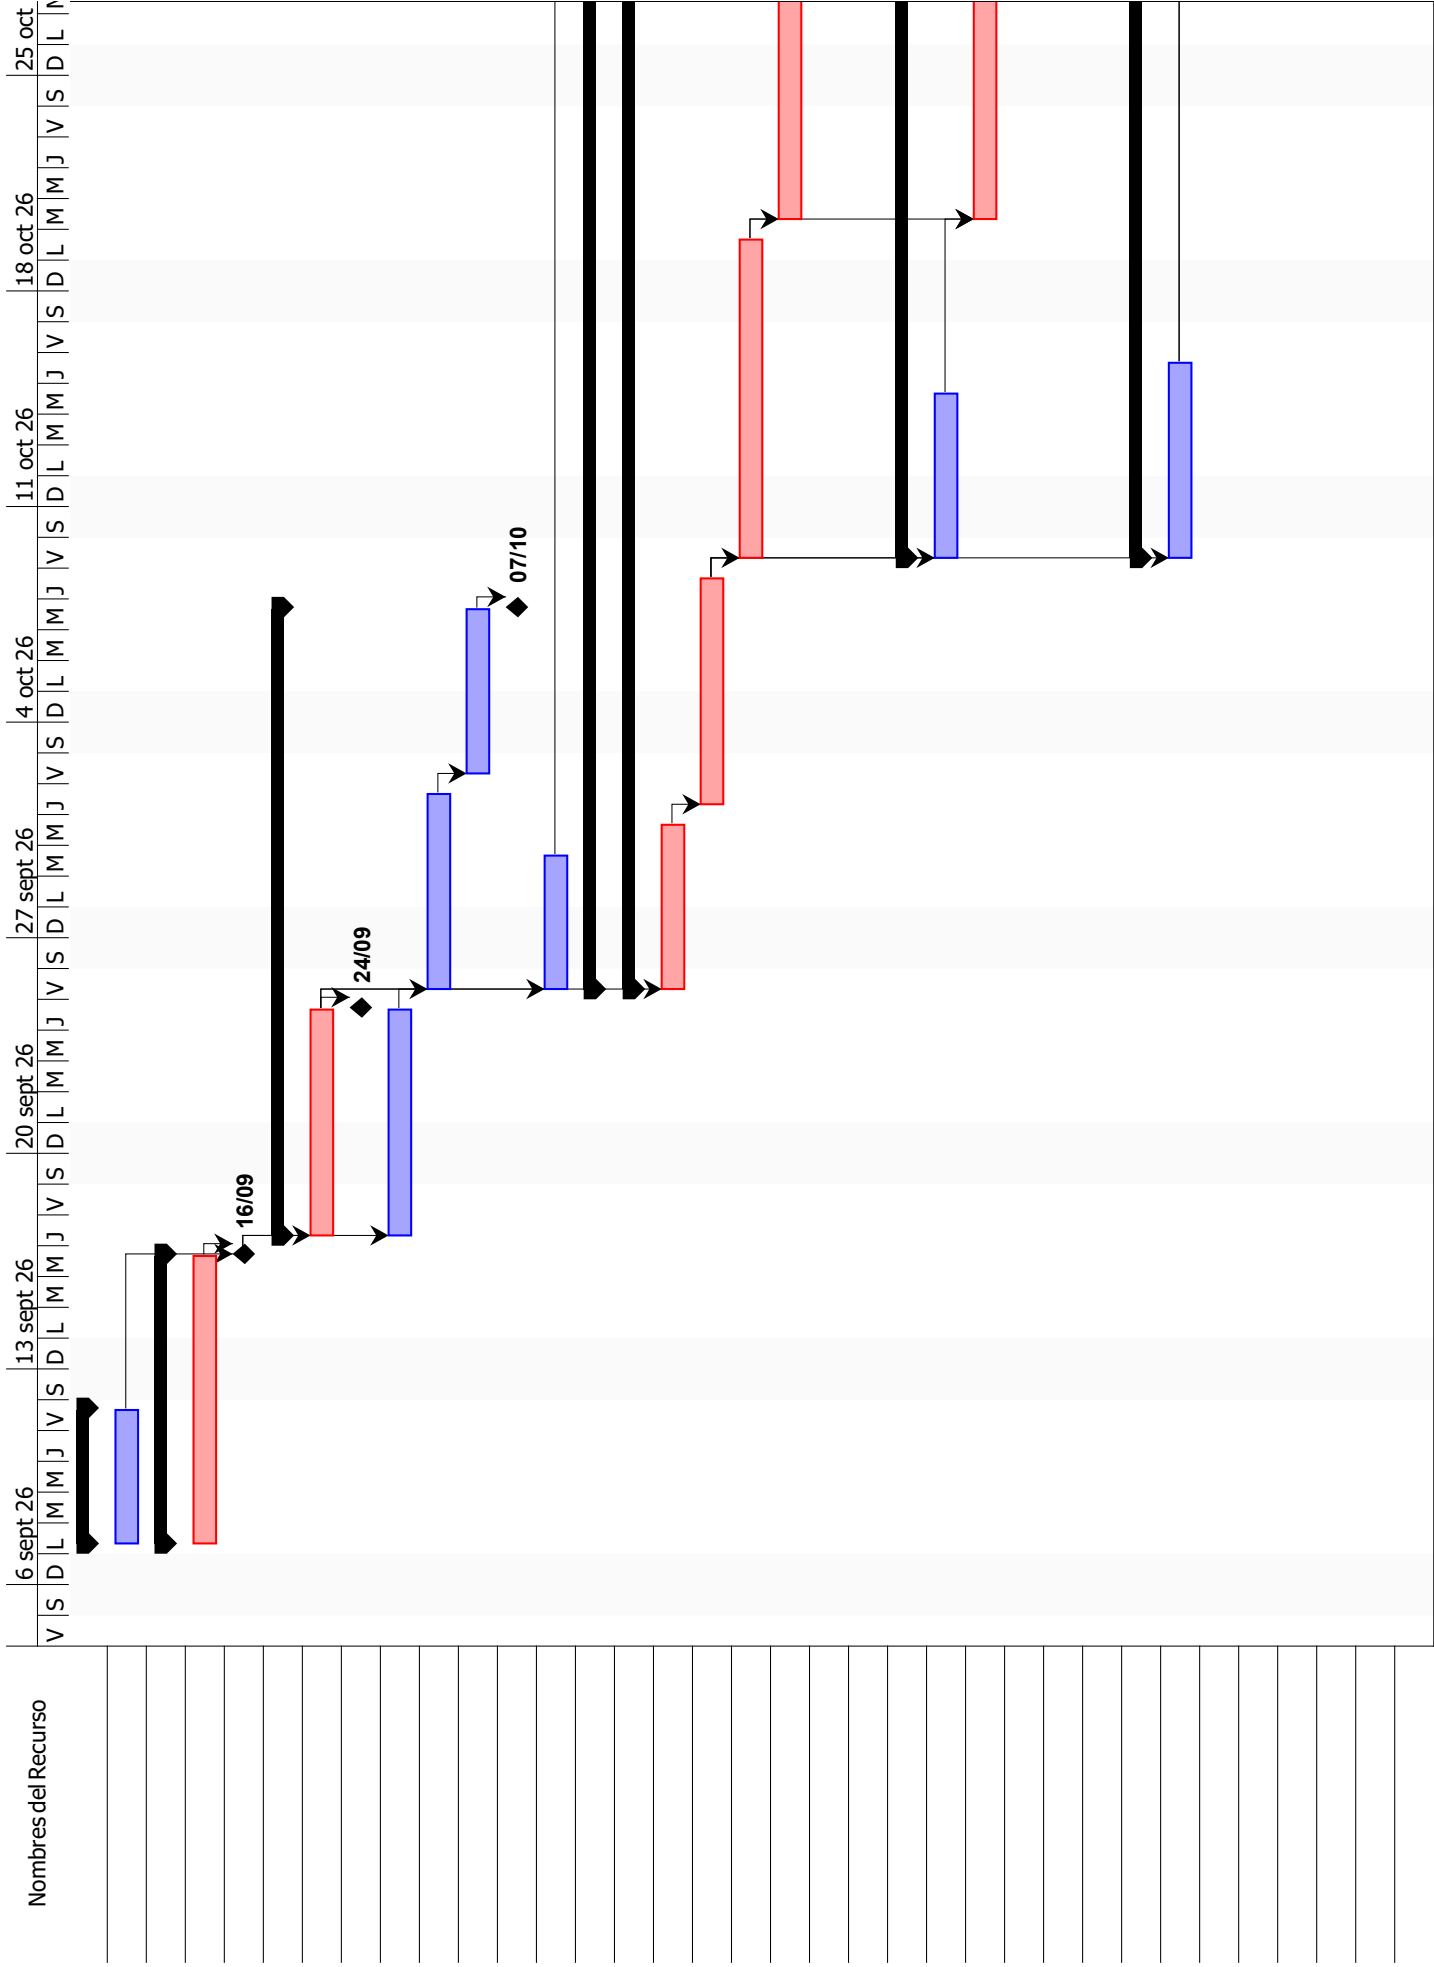

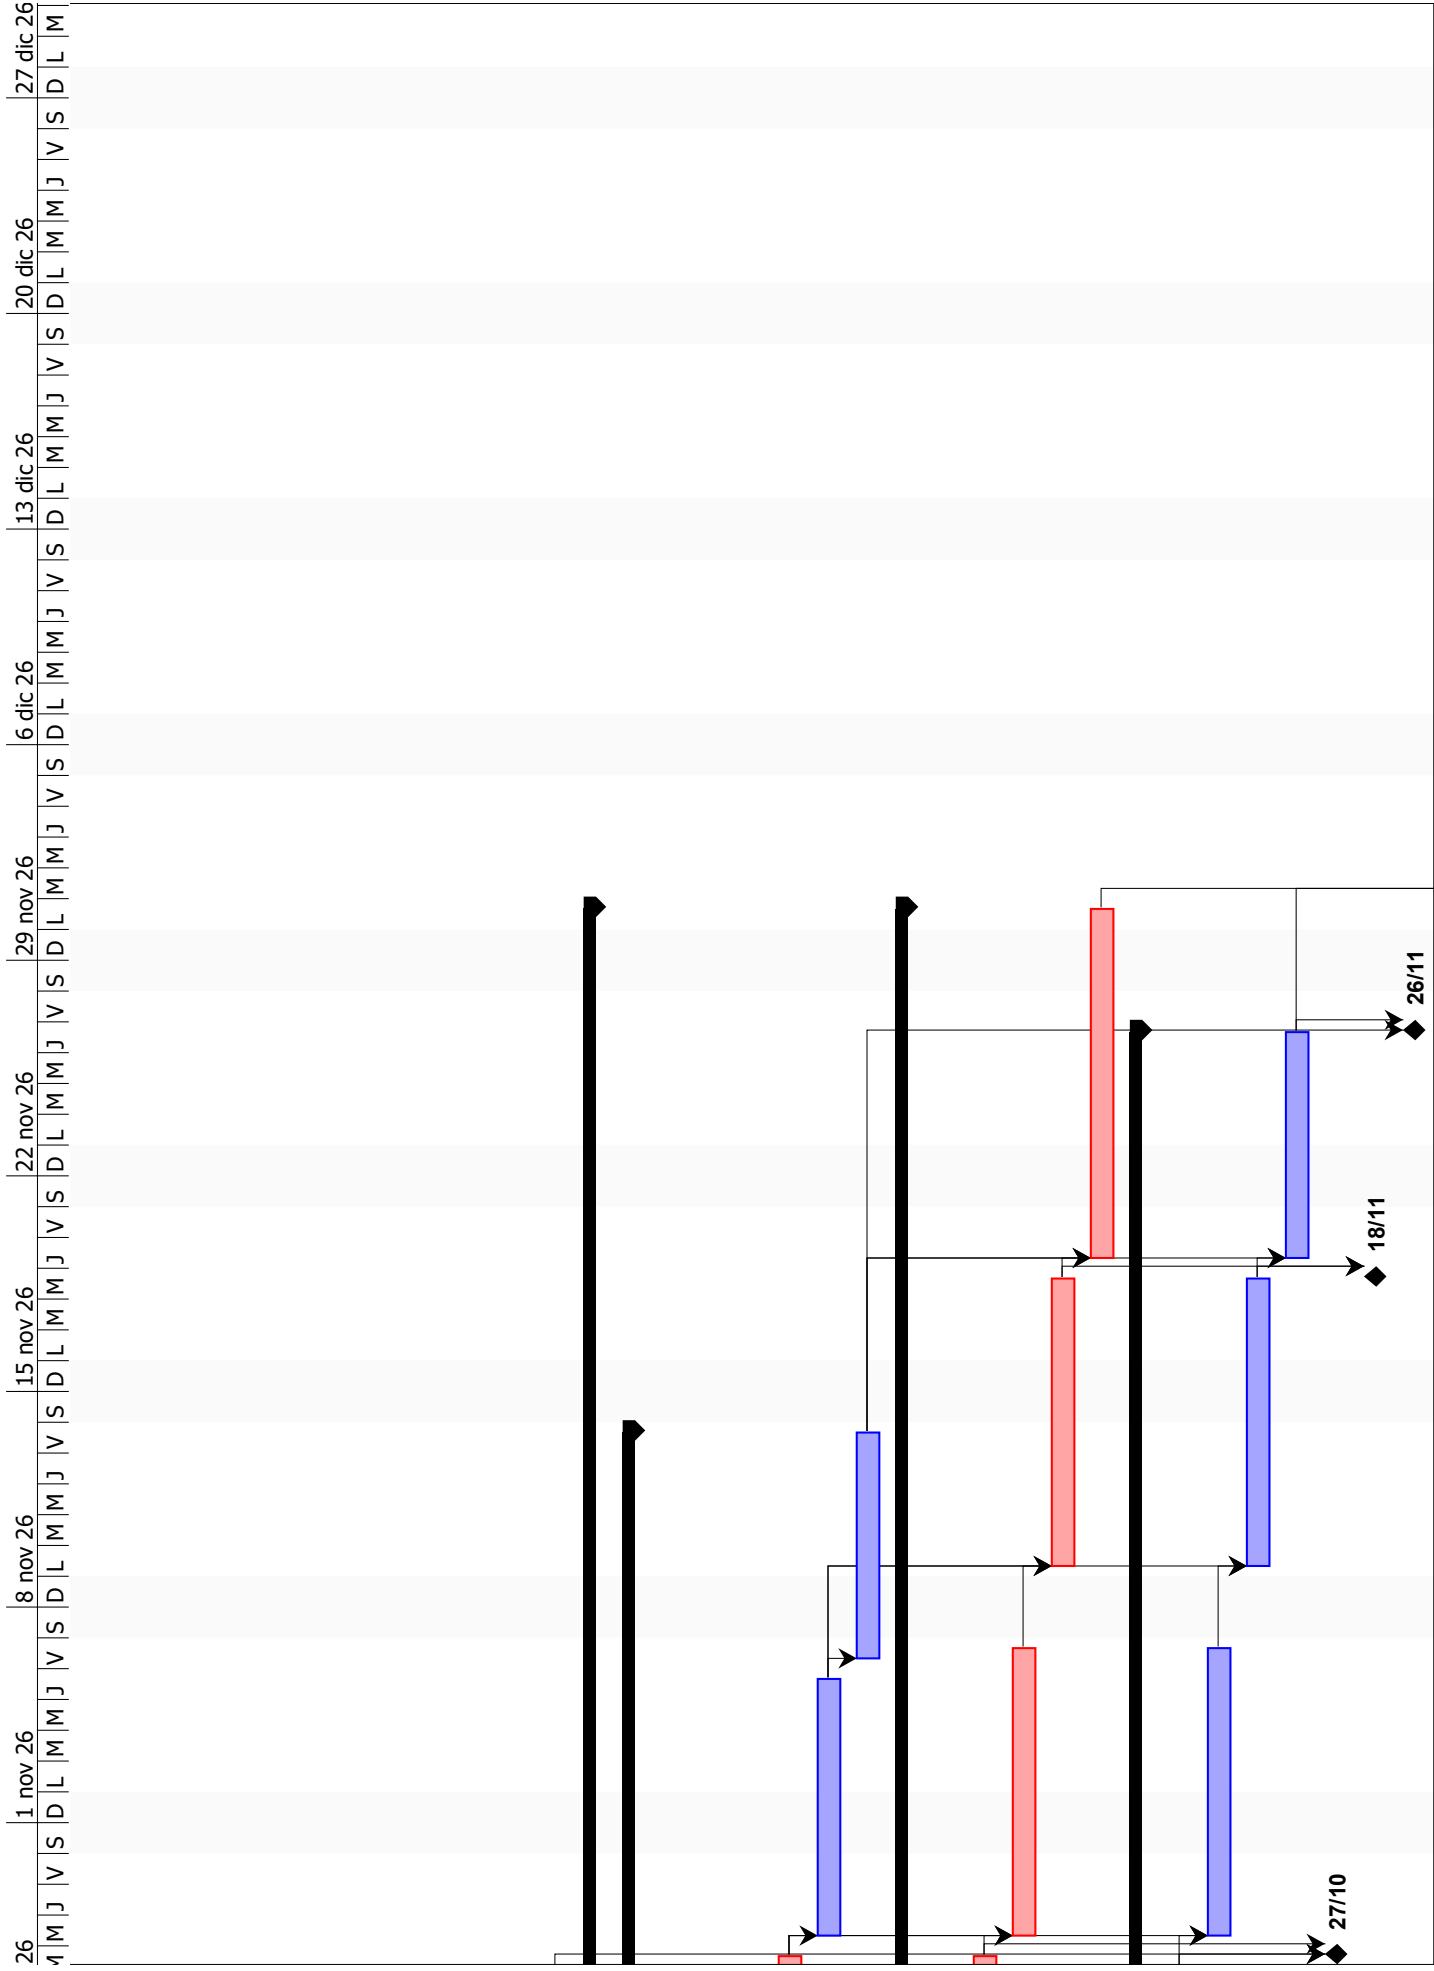

		Nombre	Duracion	Inicio	Terminado	Predecesores
36		5.0 PRUEBAS Y CONTROL DE CALIDAD	25 days	01/12/26, 08:00	04/01/27, 17:00	
37		Pruebas unitarias (Backend, Movil, Ba...	6 days	01/12/26, 08:00	08/12/26, 17:00	27,32
38		Correccion de errores encontrados	4 days	09/12/26, 08:00	14/12/26, 17:00	37
39		Pruebas de integracion Backend-App-...	4 days	15/12/26, 08:00	18/12/26, 17:00	38
40		Pruebas funcionales y de regresion	4 days	21/12/26, 08:00	24/12/26, 17:00	39
41		HITO: Despliegue a produccion (Sema...	0 days	24/12/26, 17:00	24/12/26, 17:00	40
42		Pruebas de rendimiento, carga y segu...	3 days	25/12/26, 08:00	29/12/26, 17:00	41
43		UAT e informe final de calidad	4 days	30/12/26, 08:00	04/01/27, 17:00	42
44		HITO: Pruebas de aceptacion (UAT) c...	0 days	04/01/27, 17:00	04/01/27, 17:00	43
45		6.0 DESPLIEGUE Y PUESTA EN PRODUC...	5 days	05/01/27, 08:00	11/01/27, 17:00	
46		Preparacion de infraestructura y carg...	2 days	05/01/27, 08:00	06/01/27, 17:00	44
47		Publicacion en Google Play y App Store	2 days	07/01/27, 08:00	08/01/27, 17:00	46
48		Preparacion de lanzamiento, documen...	2 days	07/01/27, 08:00	08/01/27, 17:00	46
49		Lanzamiento oficial y monitoreo post-l...	1 day	11/01/27, 08:00	11/01/27, 17:00	47,48
50		HITO: Lanzamiento oficial (Semana 16...	0 days	11/01/27, 17:00	11/01/27, 17:00	49

[illegible]

